

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(PRE-CABLING & INSTALLATION)**



Doc No.	SCC PIW(PC)	Rev. No.	1	Date	5 JUNE 2020
---------	-------------	----------	---	------	-------------

**CONTRACT TITLE :**

**PEMBEKALAN, PEMASANGAN DAN PENGUJIAN FASILITI DISTRIBUTION AUTOMATION (DA) SECARA BERSEPADU  
ZONE 2: SELANGOR**

<b>CONTRACT NO. :</b>	TNB685/2022	
<b>CONTRACTOR :</b>	EMPIRE RHEA	
<b>DATE :</b>	11-03-2025	
<b>SUBSTATION NAME :</b>	PE TAMAN DESA IDAMAN 2	
<b>FUNCTIONAL LOCATION :</b>	BBAN/PCE/J01053	
<b>SUBZONE :</b>	BANTING	
<b>STATE :</b>	SELANGOR	
<b>WORK TYPE :</b> (Tick "✓" whichever applicable)		Plant Interfacing Work (PIW) VCB
		Plant Interfacing Work (PIW) M-RMU
		INTEGRATED DA VCB
	✓	INTEGRATED DA M-RMU

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(PRE-CABLING & INSTALLATION)**



<b>Doc No.</b>	<b>SCC PIW(PC)</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A1. SCC PIW (DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

Check boxes as follows: (✓) OK NI : Need Improvement (Pls. give comments at 'Remark' column)

No.	Description	OK	NI	REMARKS
<b>1.</b>	<b>Visual Checks on RCB</b>			
i.	RCB cabinet is properly mounted & aligned at the wall / designated area.	✓		
ii.	QR code / label is available inside RCB Cabinet. The information on QR label* is scanned & checked (according to SOW) [* If available for this contract]	✓		
iii.	All wirings to the terminal blocks are terminated tightly and terminal blocks are in good condition.	✓		
iv.	All cables shall be properly glanded at the cable entry points using proper glanding and sealing (to ensure no space/gap between the cable entry points/glands and the panel)	✓		
v.	For RCB Multi-pin with Interconnector cables, inspect condition of pins (not bended/broken/'sub-merged' in the holder).	✓		
vi.	For RCB Multi-pin with Interconnector cables, check pin no. assignment with signal arrangement.	✓		
vii.	For RCB Multi-pin with Interconnector cables, check DC Earth fault to Ground.	✓		
viii.	For RCB Multi-pin with Interconnector cables, check cable support to avoid stress on the connector side.	✓		
ix.	For RCB Multi-pin with Interconnector cables, ensure cables on both ends are connected to the correct feeder number.	✓		
<b>2.</b>	<b>Visual and Physical Checks on Cablings and Terminations</b>			
i.	All non-armoured cables shall be installed in rigid high impact PVC conduits, neatly secured in position and adequately supported where necessary in an approved manner.	✓		
ii.	The size of the PVC conduit shall be 25 mm in diameter and the colour of the conduit and fittings shall be orange. The conduits shall be fixed by means of saddles secured rigidly at intervals not exceeding 750 mm.	✓		
iii.	Cable supports/brackets/elbows shall be installed at intervals not greater than 1500 mm for vertical runs and not greater than 1000 mm for horizontal runs. The brackets shall be derusted, finished in a primer and coated with standard orange enamel. The brackets/elbows shall not be painted.	✓		
iv.	For armoured cables, cable supports, elbows, cleats, trays shall be used. All materials must be of galvanised type (of at least 1.2 mm in thickness).	✓		
v.	For each termination from VCB / MRMU / EFI / Battery Charger / AC point to RCB: (i) Core number shall be marked using ferrules (ferrules shall be of one character slip-on interlocking type only). (ii) Diameter of interlocking ferrules shall be 2.5 mm & preferred brand is Partex. (iii) "TRIP" ferrules (red colour) for trip circuits. No two or more plant panels shall share a common/same cable. All cables shall be properly labelled at both ends as per signal arrangement drawings using heat shrinkable labels or cable tags.	✓		
vi.	No two or more plant panels shall share a common/same cable.	✓		

**Observations:**

Checks conducted by: Contractor's Signature & Stamp:	Verified by: TNB's Representative Signature & Stamp:
Name: HASFARRUDDIN SKAID	Name:
Date: 11-03-2025	Date:

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(PRE-CABLING & INSTALLATION)**



<b>Doc No.</b>	<b>SCC PIW(PC)</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A1. SCC PIW (DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

Check boxes as follows: (✓) OK NI : Need Improvement (Pls. give comments at 'Remark' column)

No.	Description	OK	NI	REMARKS
<b>3.</b>	<b>Visual Checks on Installations</b>			
<b>a.</b>	<b>Battery Charger (including Batteries)</b>			
i.	Mounted in stable condition & aligned at the designated area.	✓		
ii.	Use of proper Torque Wrench (11 Nm) for installation of batteries	✓		
iii.	QR Label Information is available inside Battery Charger Panel. Scanned and checked information on QR label* (according to SOW). [* If available for this contract]	✓		
<b>b.</b>	<b>Earth Fault Indicators (EFIs)</b>			
i.	Installed on a mounting board, at designated area with cable markings for each EFI.	✓		
ii.	Not more than 2 nos. of EFIs on the mounting board.	✓		
<b>4.</b>	<b>Site Drawings &amp; Tests</b>			
i.	Hardcopy of Approved Drawings - Documents are available & placed inside RCB / RTU panel. [Note: Any changes to the drawings shall be updated in softcopy and passed to TNB as As-built drawings].	✓		
ii.	Hardcopy of <b>Mastersheet &amp; Wiring List (Working Copies)</b> - Any changes shall be updated/written in the Mastersheet & Wiring List & <b>verified, signed and stamped by supervisor / representative</b> - Documents are available & placed inside RCB / RTU panel.	✓		

**Observations:**

Checks conducted by: Contractor's Signature & Stamp:	Verified by: TNB's Representative Signature & Stamp:
Name: HASFARRUDDIN SAAD	Name:
Date: 11-03-2025	Date:



**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(PRE-CABLING & INSTALLATION)**



<b>Doc No.</b>	<b>SCC PIW(PC)</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A2. PICTURES (BEFORE &amp; AFTER DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

**BEFORE INSTALLATION**

<p align="center">OVERALL PICTURE OF SUBSTATION OUTER WALL (WITH SUBSTATION NAME)</p>	<p align="center">OVERVIEW OF SWITCHGEAR (WITHOUT PRE-CABLING)</p>	<p align="center">DESIGNATED SPACE/WALL FOR REMOTE CONTROL BOX INSTALLATION</p>
<p align="center">DESIGNATED SPACE/WALL FOR BATTERY CHARGER INSTALLATION</p>	<p align="center">EXISTING EFI(S) OR DESIGNATED SPACE/WALL FOR EFI INSTALLATION</p>	<p align="center">EXISTING EFI(S) OR DESIGNATED SPACE/WALL FOR EFI INSTALLATION SECOND PIC (IF ANY)</p>

The information contained in this document is the property of Tenaga Nasional Berhad and is supplied without liability for error or omissions. No part may be reproduced or used except as authorised by contract or other written permission.

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK (PIW)  
(PRE-CABLING & INSTALLATION)**



Doc No.	SCC PIW(PC)	Rev. No.	1	Date	5 JUNE 2020
---------	-------------	----------	---	------	-------------

<b>A2. PICTURES (BEFORE &amp; AFTER DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

**AFTER INSTALLATION**

		
<p>OVERALL PICTURE OF SUBSTATION OUTER WALL (WITH SUBSTATION NAME)</p>	<p>OVERVIEW OF SWITCHGEAR (WITH COMPLETED PRE-CABLING)</p>	<p>REMOTE CONTROL BOX (AFTER INSTALLATION)</p>
		
<p>BATTERY CHARGER (AFTER INSTALLATION)</p>	<p>EF1(s) (AFTER INSTALLATION)</p>	<p>EF1(s) (AFTER INSTALLATION) SECOND PICTURE (IF ANY)</p>

The information contained in this document is the property of Tenaga Nasional Berhad and is supplied without liability for error or omissions. No part may be reproduced or used except as authorised by contract or other written permission.

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(SHUTDOWN)**



Doc No.	SCC PIW(SD)	Rev. No.	1	Date	5 JUNE 2020
---------	-------------	----------	---	------	-------------

**CONTRACT TITLE :**

**PEMBEKALAN, PEMASANGAN DAN PENGUJIAN FASILITI DISTRIBUTION AUTOMATION (DA) SECARA BERSEPADU  
ZONE 2: SELANGOR**

<b>CONTRACT NO. :</b>	TNB685/2022	
<b>CONTRACTOR :</b>	EMPIRE RHEA	
<b>DATE :</b>	17-03-2025	
<b>SUBSTATION NAME :</b>	PE TAMAN DESA IDAMAN 2	
<b>FUNCTIONAL LOCATION :</b>	BBAN/PCE/J01053	
<b>SUBZONE :</b>	BANTING	
<b>STATE :</b>	SELANGOR	
<b>WORK TYPE :</b> (Tick "✓" whichever applicable)		Plant Interfacing Work (PIW) VCB
		Plant Interfacing Work (PIW) M-RMU
		INTEGRATED DA VCB
	✓	INTEGRATED DA M-RMU

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(SHUTDOWN)**




<b>Doc No.</b>	<b>SCC PIW(SD)</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A1. SITE COMPLETION CHECKLIST FOR PLANT INTERFACING WORK (SHUTDOWN)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

Check boxes as follows: (✓) OK NI : Need Improvement (Pls. give comments at 'Remark' column)


No.	Description	OK	NI	REMARKS
<b>1.</b>	<b>Visual Checks on RCB</b>			
i.	Printed stencils (black text on white, with laminated tape) are completed and put for station name / numberings at: <ul style="list-style-type: none"> <li>Remote Control Box (RCB)'s Door Panel</li> <li>Link numbers for feeders in the RCB</li> </ul>	✓		
ii.	SCADA-ready Stickers are stucked next to Local/Remote Switches	N/A		
iii.	All feeders' labellings tally with switchgears at site.	✓		
iv.	All Local/Remote switches are at Remote position at switchgears	✓		
v.	All non-armoured cables (including EFI CT cable) shall be installed in rigid high impact PVC conduits, neatly secured in position and adequately supported where necessary in an approved manner.	✓		
vi.	All wirings to the terminal blocks are wired according to Cable Schedule, terminated tightly and terminal blocks are in good condition.	✓		
vii.	All cables shall be properly glanded at the cable entry points using proper glanding and sealing (to ensure no space/gap between the cable entry points/glands and the panel)	✓		
<b>2.</b>	<b>Visual Checks on Installations</b>			
<b>a.</b>	<b>Battery Charger (including Batteries)</b>			
i.	All wirings to the terminal blocks are terminated tightly and terminal blocks are in good condition.	✓		
ii.	Relevant Stickers for Battery Charger are available.	✓		
iii.	All tests for Battery Charger are conducted & Test results recorded in Test Forms accordingly.	✓		
<b>b.</b>	<b>Earth Fault Indicators (EFIs)</b>			
i.	Printed stencils (black text on white, with laminated tape) are available for numbering on the mounting board.	✓		
ii.	EFI CT cables from EFI to Switchgears are laid, terminated & clamped.	✓		
<b>3.</b>	<b>Site Drawings &amp; Tests</b>			
i.	Hardcopy of Approved Drawings <ul style="list-style-type: none"> <li>Documents are available &amp; placed inside RCB / RTU panel.</li> <li>[Note: Any changes to the drawings shall be <b>updated in softcopy</b> and passed to TNB as As-built drawings].</li> </ul>	✓		
ii.	Hardcopy of <b>Mastersheet &amp; Wiring List (Working Copies)</b> <ul style="list-style-type: none"> <li>Any changes shall be updated/written in the Mastersheet &amp; Wiring List &amp; <b>verified, signed and stamped by supervisor / representative</b></li> <li>Documents are available &amp; placed inside RCB / RTU panel.</li> </ul>	✓		
iii.	Check & verify all necessary tests are performed as required & have passed.	✓		

**Observations:**

Checks conducted by: Contractor's Signature & Stamp:	Verified by: TNB's Representative Signature & Stamp:
	
Name: HASFARRUDDIN SKAID	Name:
Date: 17-03-2025	Date:

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(SHUTDOWN)**



<b>Doc No.</b>	<b>SCC PIW(SD)</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A1. SCC PIW (DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			
Remote Control Box	Brand	MULTIPIN INDKOM			
	Type	Multipin	✓	Conventional	
	Serial Number	RCB 1 Serial Number	2405405		
		RCB 2 Serial Number			
RCB 3 Serial Number					
Battery Charger	Brand	SUNPOWER			
	Serial Number	11193-8054			
Earth Fault Indicator	Serial Number	EFI-1:	1572371	EFI-6:	
		EFI-2:	1572368	EFI-7:	
		EFI-3:		EFI-8:	
		EFI-4:		EFI-9:	
		EFI-5:		EFI-10:	
Switchgear	Brand	INDKOM			
	Configuration:	2+1			
<b>Observations:</b>					
Checks conducted by: Contractor's Signature & Stamp:			Verified by: TNB's Representative Signature & Stamp:		
					
Name: HASFARRUDDIN SAAD			Name:		
Date: 17-03-2025			Date:		

**SITE COMPLETION CHECKLIST  
PLANT INTERFACING WORK(PIW)  
(SHUTDOWN)**




Doc No.	SCC PIW(SD)	Rev. No.	1	Date	5 JUNE 2020
CONTRACT NO. :		TNB685/2022			
FUNCTIONAL LOCATION :		BBAN/PCE/J01053			
SUBSTATION NAME :		PE TAMAN DESA IDAMAN 2			

Note: Please sketch the building layout and the location of:

- a. RCB panel
- b. Battery Charger
- c. EFIs location
- d. Switchgear Panel
- e. RTU Panel

**SITE DRAWING:**

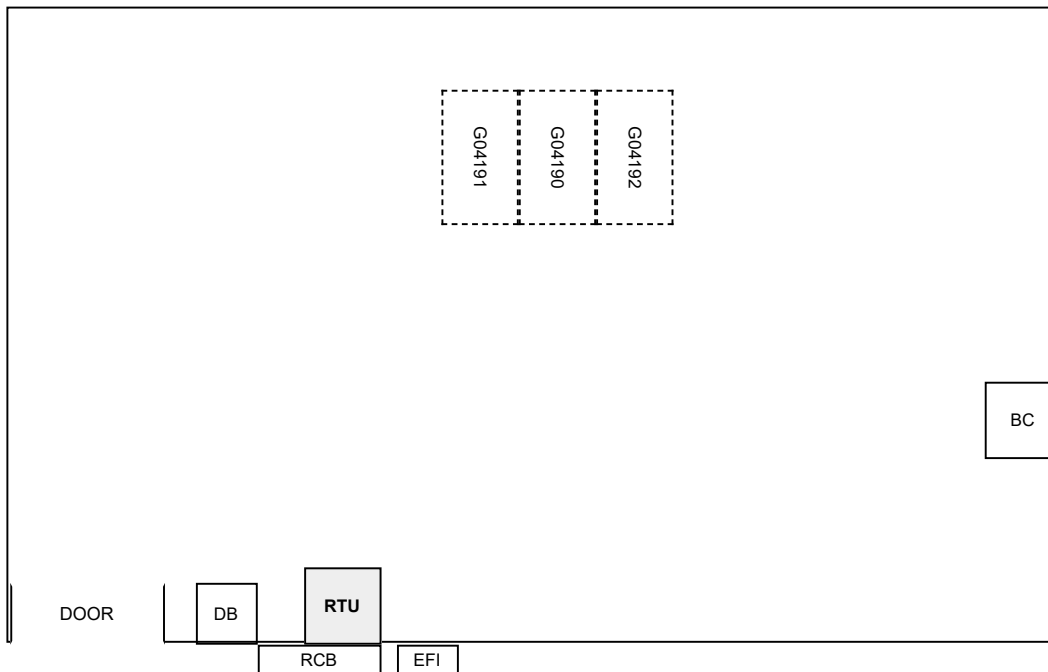

**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



Doc No.	SAT PIW - VCB	Rev. No.	1	Date	5 JUNE 2020
---------	---------------	----------	---	------	-------------

**CONTRACT TITLE :**

**PEMBEKALAN, PEMASANGAN DAN PENGUJIAN FASILITI DISTRIBUTION AUTOMATION (DA) SECARA BERSEPADU  
ZONE 2: SELANGOR**

<b>CONTRACT NO. :</b>	<b>TNB685/2022</b>
<b>CONTRACTOR :</b>	<b>EMPIRE RHEA</b>
<b>DATE :</b>	<b>17-03-2025</b>
<b>SUBSTATION NAME :</b>	<b>PE TAMAN DESA IDAMAN 2</b>
<b>FUNCTIONAL LOCATION :</b>	<b>BBAN/PCE/J01053</b>
<b>SUBZONE :</b>	<b>BANTING</b>
<b>STATE :</b>	<b>SELANGOR</b>

**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



Doc No.	SAT PIW - VCB	Rev. No.	1	Date	5 JUNE 2020
---------	---------------	----------	---	------	-------------

**A5. TERMINATION CONTINUITY TEST (RCB MULTIPIN INDKOM)**

4. Conduct Point-to-point Cable Termination Continuity Tests.
5. Conduct Short to Ground (Leakage) test for each connector pin.
6. Record test results in [1] Termination Continuity Test Sheet.

**[1] TERMINATION CONTINUITY TEST SHEET**

**Feeder No.:** G014191  
**Feeder Name:** JLN MERBAH KELABU 27

19 cores, 1.5 mm sq, armoured (Alarm & Control cables) \*Note: Please add/edit according to station's requirement

Cable No.	Core No.	Signal	From	To	Termination Continuity Test	Short to Ground (Leakage) Test	REMARKS
1A	1	Earth	RCB	SG PANEL	✓	Not applicable	
1A	2	Gas Alarm	RCB	SG PANEL	✓	✓	
1A	3	Spare	RCB	SG PANEL	✓	✓	
1A	4	LBS/CB Open Point	RCB	SG PANEL	✓	✓	
1A	5	LBS/CB Close Point	RCB	SG PANEL	✓	✓	
1A	6	Earth Switch Open Point	RCB	SG PANEL	✓	✓	
1A	7	Earth Switch Close Point	RCB	SG PANEL	✓	✓	
1A	8	Common -ve from Plant	RCB	SG PANEL	✓	✓	
1A	9	Remote/Supervisory Status	RCB	SG PANEL	✓	✓	
1A	10	Trip Circuit Supervisor / Spare	RCB	SG PANEL	✓	✓	
1A	11	Overcurrent / Spare	RCB	SG PANEL	✓	✓	
1A	12	Earth Fault / Spare	RCB	SG PANEL	✓	✓	
1A	13	RF Status / Spare	RCB	SG PANEL	✓	✓	
1A	14	Current Diff / Spare	RCB	SG PANEL	✓	✓	
1A	15	Common -ve from RTU	RCB	SG PANEL	✓	✓	
1A	16	Common from Plant (Close CCT)	RCB	SG PANEL	✓	✓	
1A	17	Common Close From R/S	RCB	SG PANEL	✓	✓	
1A	18	Common from Plant (Open CCT)	RCB	SG PANEL	✓	✓	
1A	19	Common Open From R/S	RCB	SG PANEL	✓	✓	

2-pair, twisted, 1.5 mm sq, armoured (Analog cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
1B		Amp +	RCB	SG PANEL	✓	
1B		Amp -	RCB	SG PANEL	✓	
1B		Spare	RCB	SG PANEL		
1B		Spare	RCB	SG PANEL		

4 cores, 1.0 mm sq, non-armoured (EFI signal cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
EF11	1	Common	EFI	RCB	✓	
EF11	2	EFI Indication	EFI	RCB	✓	
EF11	3	CO-Common	EFI	RCB	✓	
EF11	4	EFI Reset	EFI	RCB	✓	

Test Observations:


**Test Result: PASS  FAIL**

Checks conducted by:  
Contractor's Signature & Stamp:

Verified by:  
TNB's Representative Signature & Stamp:

Name: HASFARRUDDIN SAID  
Date: 17-03-2025

Name:  
Date:



**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



**Doc No.** SAT PIW - VCB      **Rev. No.** 1      **Date** 5 JUNE 2020

**A5. TERMINATION CONTINUITY TEST (RCB MULTIPIN INDKOM)**

4. Conduct Point-to-point Cable Termination Continuity Tests.
5. Conduct Short to Ground (Leakage) test for each connector pin.
6. Record test results in [1] **Termination Continuity Test Sheet**.

**[1] TERMINATION CONTINUITY TEST SHEET**

**Feeder No.:** G014190  
**Feeder Name:** PDT TMN MERPATI

19 cores, 1.5 mm sq, armoured (Alarm & Control cables) \*Note: Please add/edit according to station's requirement

Cable No.	Core No.	Signal	From	To	Termination Continuity Test	Short to Ground (Leakage) Test	REMARKS
2A	1	Earth	RCB	SG PANEL	✓	Not applicable	
2A	2	Gas Alarm	RCB	SG PANEL	✓	✓	
2A	3	Spare	RCB	SG PANEL	✓	✓	
2A	4	LBS/CB Open Point	RCB	SG PANEL	✓	✓	
2A	5	LBS/CB Close Point	RCB	SG PANEL	✓	✓	
2A	6	Earth Switch Open Point	RCB	SG PANEL	✓	✓	
2A	7	Earth Switch Close Point	RCB	SG PANEL	✓	✓	
2A	8	Common -ve from Plant	RCB	SG PANEL	✓	✓	
2A	9	Remote/Supervisory Status	RCB	SG PANEL	✓	✓	
2A	10	Trip Circuit Supervisor / Spare	RCB	SG PANEL	✓	✓	
2A	11	Overcurrent / Spare	RCB	SG PANEL	✓	✓	
2A	12	Earth Fault / Spare	RCB	SG PANEL	✓	✓	
2A	13	RF Status / Spare	RCB	SG PANEL	✓	✓	
2A	14	Current Diff / Spare	RCB	SG PANEL	✓	✓	
2A	15	Common -ve from RTU	RCB	SG PANEL	✓	✓	
2A	16	Common from Plant (Close CCT)	RCB	SG PANEL	✓	✓	
2A	17	Common Close From R/S	RCB	SG PANEL	✓	✓	
2A	18	Common from Plant (Open CCT)	RCB	SG PANEL	✓	✓	
2A	19	Common Open From R/S	RCB	SG PANEL	✓	✓	

2-pair, twisted, 1.5 mm sq, armoured (Analog cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
2B		Amp +	RCB	SG PANEL	✓	
2B		Amp -	RCB	SG PANEL	✓	
2B		Spare	RCB	SG PANEL		
2B		Spare	RCB	SG PANEL		

4 cores, 1.0 mm sq, non-armoured (EFI signal cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
EF12	1	Common	EFI	RCB	✓	
EF12	2	EFI Indication	EFI	RCB	✓	
EF12	3	CO-Common	EFI	RCB	✓	
EF12	4	EFI Reset	EFI	RCB	✓	

Test Observations:


**Test Result: PASS**  **FAIL**

Checks conducted by:  
Contractor's Signature & Stamp:

Verified by:  
TNB's Representative Signature & Stamp:

Name: HASFARRUDDIN SAID  
Date: 17-03-2025

Name:  
Date:



**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



Doc No.	SAT PIW - VCB	Rev. No.	1	Date	5 JUNE 2020
---------	---------------	----------	---	------	-------------

**A5. TERMINATION CONTINUITY TEST (RCB MULTIPIN INDKOM)**

4. Conduct Point-to-point Cable Termination Continuity Tests.
5. Conduct Short to Ground (Leakage) test for each connector pin.
6. Record test results in [1] **Termination Continuity Test Sheet**.

**[1] TERMINATION CONTINUITY TEST SHEET**

**Feeder No.:** G014192

**Feeder Name:** TX300KVA

19 cores, 1.5 mm sq, armoured (Alarm & Control cables) \*Note: Please add/edit according to station's requirement

Cable No.	Core No.	Signal	From	To	Termination Continuity Test	Short to Ground (Leakage) Test	REMARKS
3A	1	Earth	RCB	SG PANEL	✓	Not applicable	
3A	2	Gas Alarm	RCB	SG PANEL	✓	✓	
3A	3	Spare	RCB	SG PANEL	✓	✓	
3A	4	LBS/CB Open Point	RCB	SG PANEL	✓	✓	
3A	5	LBS/CB Close Point	RCB	SG PANEL	✓	✓	
3A	6	Earth Switch Open Point	RCB	SG PANEL	✓	✓	
3A	7	Earth Switch Close Point	RCB	SG PANEL	✓	✓	
3A	8	Common -ve from Plant	RCB	SG PANEL	✓	✓	
3A	9	Remote/Supervisory Status	RCB	SG PANEL	✓	✓	
3A	10	Trip Circuit Supervisor / Spare	RCB	SG PANEL	✓	✓	
3A	11	Overcurrent / Spare	RCB	SG PANEL	✓	✓	
3A	12	Earth Fault / Spare	RCB	SG PANEL	✓	✓	
3A	13	RF Status / Spare	RCB	SG PANEL	✓	✓	
3A	14	Current Diff / Spare	RCB	SG PANEL	✓	✓	
3A	15	Common -ve from RTU	RCB	SG PANEL	✓	✓	
3A	16	Common from Plant (Close CCT)	RCB	SG PANEL	✓	✓	
3A	17	Common Close From R/S	RCB	SG PANEL	✓	✓	
3A	18	Common from Plant (Open CCT)	RCB	SG PANEL	✓	✓	
3A	19	Common Open From R/S	RCB	SG PANEL	✓	✓	

2-pair, twisted, 1.5 mm sq, armoured (Analog cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
3B		Amp +	RCB	SG PANEL	✓	
3B		Amp -	RCB	SG PANEL	✓	
3B		Spare	RCB	SG PANEL		
3B		Spare	RCB	SG PANEL		

4 cores, 1.0 mm sq, non-armoured (EFI signal cables)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
EF13	1	Common	EFI	RCB	✓	
EF13	2	EFI Indication	EFI	RCB	✓	
EF13	3	CO-Common	EFI	RCB	✓	
EF13	4	EFI Reset	EFI	RCB	✓	

Test Observations:

**Test Result: PASS  FAIL**

Checks conducted by:  
Contractor's Signature & Stamp:


Verified by:  
TNB's Representative Signature & Stamp:

Name: HASFARRUDDIN SAID

Name:

Date: 17-03-2025

Date:



**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



Doc No.	SAT PIW - VCB	Rev. No.	1	Date	5 JUNE 2020
---------	---------------	----------	---	------	-------------

**A1. TERMINATION CONTINUITY TEST (RCB MULTIPIN INDKOM)**

1. Conduct Point-to-point Cable Termination Continuity Tests.
2. Record test results in [1] Termination Continuity Test Sheet.

[1]	TERMINATION CONTINUITY TEST SHEET
PE Name:	PE TAMAN DESA IDAMAN 2

4 cores, 4 mm sq (coloured armoured) - AC cable for Battery Charger

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
AC-BC1	RED	Line	DB	BC	✓	
AC-BC1	BLUE	Neutral	DB	BC	✓	
AC-BC1	YELLOW	Earth	DB	BC	✓	
AC-BC1	BLACK	Spare	DB	BC	✓	

4 cores, 1.5 mm sq, armoured (Battery Charger alarms)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
BC1	1	Common	BC	RCB	✓	
BC1	2	Battery Charger Alarm 1	BC	RCB	✓	
BC1	3	Common	BC	RCB	✓	
BC1	4	AC Fail	BC	RCB	✓	
BC2	1	Common	BC	RCB	✓	
BC2	2	Battery Charger Alarm 1	BC	RCB	✓	
BC2	3	Common	BC	RCB	✓	
BC2	4	AC Fail	BC	RCB	✓	

2 cores, 2.5 mm sq, armoured (DC Cable)

Cable No.	Core No.	Signal	From	To	Test Result	REMARKS
BC1 - RCB	RED	+30VDC	BC	RCB	✓	
BC1 - RCB	BLACK	-30VDC	BC	RCB	✓	

Test Observations:

Test Result: PASS  FAIL

Checks conducted by:  
Contractor's Signature & Stamp:

Verified by:  
TNB's Representative Signature & Stamp:

Name: HASFARRUDDIN SAID

Name:

Date: 17-03-2025

Date:



**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



Doc No.	SAT PIW - VCB	Rev. No.	1	Date	5 JUNE 2020
---------	---------------	----------	---	------	-------------

**A2. RCB CONTROL OPERATION INTERLOCK TEST**

1. Conduct Point-to-point Cable Termination Continuity Tests.
2. Record test results in [1] Termination Continuity Test Sheet.

[2]	RCB CONTROL OPERATION INTERLOCK TEST SHEET				
PE Name:	PE TAMAN DESA IDAMAN 2				
RCB brand:	MULTIPIN INDKOM				
RCB type:	RCB Conventional		RCB Multi-pin		✓

**Test Conditions:**

- The Earth Switch is at ON position (at all times) during the tests.
- The test is conducted with the breaker at half-racked in position at the VCB switchgear cubicle (Test Position)
- The breaker Test Plug is inserted into the switchgear cubicle connector to activate the Control Operation..
- To connect 30 Vdc supply for status indication change at RCB (from dry contact to wet contact)

1. Test Conducted at the Switchgear:

Breaker Local/Remote Position	Breaker Trip/Close Switch		Test Result ("✓" Passed / "X" Failed)
	TRIP	CLOSE	
LOCAL	✓	✓	✓
REMOTE	X	X	✓

2. Test Conducted at the RCB

Breaker L/R Position	RCB R/S Position	RCB Trip/Close Switch		Test Result ("✓" - Passed / "X" - Failed)
		TRIP	CLOSE	
LOCAL	REMOTE	X	X	✓
LOCAL	SUPERVISORY	X	X	✓
REMOTE	REMOTE	✓	✓	✓
REMOTE	SUPERVISORY	X	X	✓

Test Observations:

Test Result: **PASS**  **FAIL**

Checks conducted by:  
Contractor's Signature & Stamp:

Verified by:  
TNB's Representative Signature & Stamp:

Name: HASFARRUDDIN SAID (808734-A)

Date: 17-03-2025

Name:

Date:





Nama Aktiviti: PENGUJIAN MULATUGAS SISTEM 30VDC LOW MAINTENANCE

Pencawang	: PE TAMAN DESA IDAMAN 2	Jenama charger / model	: SUNPOWER
Tarikh Mulatugas	: 17-03-2025	Serial no charger	: 11193-8054
Bilangan Charger	: 1	Bulan/Tahun Penghantaran	: 2024-07
Kegunaan DC	: RMU	Jenama bateri / model	: SAFT UP1M40-4
Jika VCB, Bilangan VCB	:	Bulan/Tahun Pembuatan	: 2024-07

Activiti	Keterangan Aktiviti		Tindakan (✓)
1	Pastikan sistem DC telah siap dipasang kecuali kabel dari pengecas ke bateri & pengecas ke beban.		✓
2	Pastikan semua MCB pada pengecas bateri dalam keadaan terbuka (OFF).		✓
Activiti	Keterangan Aktiviti	Julat Bacaan	Ambil Bacaan
3	Semak bacaan voltan pembekal masuk AC (L-N) pada terminal blok pengecas bateri.	216 - 252 Vac	240
Activiti	Keterangan Aktiviti		Tindakan (✓)
4	Pastikan Suis Mode berada dalam kedudukan Manual. Hidupkan (ON) MCB AC, Bateri & Beban.		✓
Activiti	Keterangan Aktiviti	Julat Bacaan	Ambil Bacaan
5	Pastikan LED Manual Float menyala. Ukur voltan pada terminal blok ke beban.	27 - 31.5 Vdc (terminal positive ke negative)	29.4
6	Pusingkan suis ke Boost. Pastikan LED Manual Boost menyala. Ukur voltan pada terminal blok ke beban.	27 - 31.5 Vdc (terminal positive ke negative)	30.1
<b>"Jika julat voltan untuk Float atau Boost tidak dipatuhi, matikan (OFF) semua MCB. Laporkan dalam Sistem Maklumbalas Bahan(SMB) &amp; hubungi pihak pembekal untuk pembaikan segera ditapak. "</b>			
Activiti	Keterangan Aktiviti		Tindakan (✓)
7	Pusing semula suis ke Float. Pastikan LED Manual Float menyala.		✓
Activiti	Keterangan Aktiviti		Tindakan (✓)
8	<b>TEMPERATURE COMPENSATION (Float CHARGE MODE)</b> Rekodkan juga bacaan & keputusan aktiviti 8(i) hingga 8(iv) pada pelekat mulatugas pada pintu pengecas.	i) Ambil bacaan voltan pengecas bateri pada terminal blok ke bateri.	32.9
		ii) Rekod bacaan suhu pada paparan LCD.	34.8
		iii) Rujuk Jadual Temperature Compensation pada pintu pengecas & rekodkan voltan Float Min & Max.	MIN 32.74 MAX 33.4
		iv) Adakah voltan 8(i) dalam julat voltan Float Min & Max? Ya(✓) atau Tidak(X)	✓
Activiti	Keterangan Aktiviti		Tindakan (✓)
9	Pusingkan suis ke Boost. Pastikan LED Manual Boost menyala.		✓
Activiti	Keterangan Aktiviti		Tindakan (✓)
10	<b>TEMPERATURE COMPENSATION (Boost CHARGE MODE)</b> Rekodkan juga bacaan & keputusan aktiviti 10(i) hingga 10(iv) pada pelekat mulatugas pada pintu pengecas."	i) Ambil bacaan voltan pengecas bateri pada terminal blok ke bateri.	33.6
		ii) Rekod bacaan suhu pada paparan LCD.	34.8
		iii) Rujuk Jadual Temperature Compensation pada pintu pengecas & rekodkan voltan Boost Min & Max.	MIN 33.38 MAX 34.04
		iv) Adakah voltan 10(i) dalam julat voltan Boost Min & Max? Ya(✓) atau Tidak(X)	✓
<b>"Jika julat voltan untuk Float atau Boost pada no 8(iv) &amp; 10(iv) tidak dipatuhi, laporkan dalam Sistem Maklumbalas Bahan(SMB) &amp; hubungi pihak pembekal untuk pembaikan segera ditapak. Jika julat voltan untuk Float &amp; Boost dipatuhi, teruskan ke langkah seterusnya."</b>			
Activiti	Keterangan Aktiviti		Tindakan (✓)
11	Matikan (OFF) MCB pada pengecas bateri ke bateri & beban.		✓
12	Lengkapkan sambungan kabel dari pengecas ke bateri & pengecas ke beban.		✓
13	Hidupkan (ON) semula MCB pada pengecas bateri ke bateri & beban.		✓
14	Pusing suis Charger Selector Mode ke Manual & Boost. Pusing semula ke Auto. Pastikan LED Charger Auto Boost menyala.		✓
<b>Pengecas akan bertukar ke Float secara Otomatik selepas 12 Jam.</b>			

: HASFARRUDDIN SAAID

Diuji Oleh

Disahkan Oleh

Tarikh : 17-03-2025

Tarikh : 17-03-2025


Analisa/Catatan

Keputusan

Perlu Tindakan Lanjutan

Tindakan Oleh

Tarikh





**SENARAI SEMAK DAN UJIAN EFI UNTUK PROJEK DA / RECOMMISSION**

Pencawang : PE TAMAN DESA IDAMAN 2  
 LITAR : INCOMING G04191 OUTGOING G04190  
 NO. SIRI : 1572371 OUTGOING 1572368  
 JENIS EFI : EMG OUTGOING EMG

No	Ujian	Incoming	Outgoing	Komen
1	Test Kelip. Adakah EFI berfungsi dengan baik?	OK	OK	Lakukan test dan reset pada EFI tersebut. Untuk EFI endau semak External Indicator.
2	Adakah terdapat LV SUPPLY (230V) tersambung pada EFI?	OK	OK	Untuk jenama Cableroll 2310, jika tiada LV dipasang, perlu OFF kan bit 6 & 7
3	Bacaan bateri EFI : 3.6V Adakah bacaan voltan <3.0V?	OK	OK	Jika bacaan <3.0V bateri perlu ditukar
4	Ukurkan rintangan pada terminal CT pada EFI. Adakah CT yang terpasang pada kedudukan betul?	OK	OK	Sila lihat Lampiran 2 bagi contoh pemasangan CT yang betul. Nota: untuk menyemak penyambungan CT ke terminal EFI; bacaan dalam 20-30Ω atau kurang dari 100Ω (Cableroll & Endau) / 2.4kΩ (EMG)
5	Jalankan ujian secondary current injection pada CT menggunakan set Bowdens	OK	OK	Satu lilitan adalah arus sebanyak 10 A
6	Gunakan buzzer dan probe pada NO	OK	OK	Ada continuity jika jalankan current injection. Perlu keluarkan jumper jika ada

Tandakan 1 = Kedudukan bit pada DIP suis pada ON  
 Tandakan 0 = Kedudukan bit pada DIP suis pada OFF  
 (sila rujuk Lampiran 4 untuk definisi setiap bit)

Endau		
BIT NO	INC	OUT
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		
11		
12		

Soule Bardin			
	BIT NO	INC	OUT
S1 DIP SUIS	1		
	2		
	3		
	4		
S2 DIP SUIS	1		
	2		
	3		
	4		
	5		


CableTroll						
BIT NO	INC	OUT		Kedudukan	INC	OUT
1				1		
2				2		
3				3		
4				4		
5				5		
6				6		

EMG Easi-R						
DIP SUIS 1 (ATAS)	INC	OUT		DIP SUIS 1 (BAWAH)	INC	OUT
1	0	0		1	0	0
2	0	0		2	0	0
3	0	0		3	1	1
4	1	1		4	0	0
5	0	0		5	0	0
6	1	1		6	1	1

**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



<b>Doc No.</b>	<b>SAT PIW - VCB</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
<b>A2. PICTURES (BEFORE &amp; AFTER DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

 <p>17/05/2025 16:22 2.83725587N 101.56648455E Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 17:53 2.83725098N 101.56642363E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 17:53 2.83725668N 101.5664726E Kampung Sungai Lempit Banting Selangor</p>
OVERALL PICTURE OF SUBSTATION OUTER WALL (WITH SUBSTATION NAME)	SAMPLE OF COMPLETED MULTI-CORE CABLE TERMINATION (AT SWITCHGEAR'S SIDE)	SAMPLE OF COMPLETED MULTI-CORE CABLE TERMINATION (INSIDE RCB)
 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>
SAMPLE OF COMPLETED MULTI-CORE CABLE TERMINATION (INSIDE RCB) SECOND PICTURE (IF ANY)	SAMPLE OVERVIEW OF RCB'S SINGLE LINE DIAGRAM (COMPLETE WITH FEEDER NUMBERS)	SAMPLE OVERVIEW OF RCB'S SINGLE LINE DIAGRAM (COMPLETE WITH FEEDER NUMBERS) SECOND PICTURE (IF ANY)
 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>	 <p>17/05/2025 16:03 2.83725918N 101.56642777E 2/3 Jalan Bukit Perah Kampung Sungai Lempit Banting Selangor</p>
OVERALL PICTURE OF WIRING LIST INSIDE RCB PANEL	OVERALL PICTURE OF RCB SCHEMATIC DIAGRAM INSIDE RCB PANEL	RCB (COMPLETE WARRANTY STICKER)

The information contained in this document is the property of Tenaga Nasional Berhad and is supplied without liability for error or omissions. No part may be reproduced or used except as authorised by contract or other written permission.

**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**






<b>Doc No.</b>	<b>SAT PIW - VCB</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
----------------	----------------------	-----------------	----------	-------------	--------------------

<b>A2. PICTURES (BEFORE &amp; AFTER DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

		
OVERVIEW OF EFI(s) AFTER INSTALLATION	OVERVIEW OF EFI(s) AFTER INSTALLATION SECOND PICTURE (IF ANY)	OVERVIEW OF EFI(s) AFTER INSTALLATION THIRD PICTURE (IF ANY)

		
SAMPLE EFI'S CT CABLE AT SWITCHGEAR (AFTER CLAMPED)	SAMPLE EFI'S CT CABLE AT SWITCHGEAR (AFTER CLAMPED) SECOND PICTURE (IF ANY)	SAMPLE EFI'S CT CABLE AT SWITCHGEAR (AFTER CLAMPED) THIRD PICTURE (IF ANY)

		
BATTERY CHARGER (COMPLETE WARRANTY STICKER)	OVERVIEW OF BATTERY CHARGER (COMPLETE WITH 30VDC LOW MAINTENANCE SYSTEM COMMISSIONING CHECKLIST) INSIDE BATTERY CHARGER	INDIVIDUAL EARTHING CONNECTIONS COMPLETED FOR I/O CABLES TO EARTH STUD AT RCB PANEL

The information contained in this document is the property of Tenaga Nasional Berhad and is supplied without liability for error or omissions. No part may be reproduced or used except as authorised by contract or other written permission.

**SITE ACCEPTANCE TEST (SAT)  
PLANT INTERFACING WORK (PIW) VCB - SHUTDOWN**



<b>Doc No.</b>	<b>SAT PIW - VCB</b>	<b>Rev. No.</b>	<b>1</b>	<b>Date</b>	<b>5 JUNE 2020</b>
----------------	----------------------	-----------------	----------	-------------	--------------------

<b>A2. PICTURES (BEFORE &amp; AFTER DURING PRE-CABLING &amp; INSTALLATION)</b>					
<b>CONTRACT NO. :</b>		TNB685/2022			
<b>FUNCTIONAL LOCATION :</b>		BBAN/PCE/J01053			
<b>SUBSTATION NAME :</b>		PE TAMAN DESA IDAMAN 2			

<p>INDIVIDUAL EARTHING CONNECTIONS COMPLETED FOR I/O CABLES TO EARTH STUD AT RCB PANEL SECOND PICTURE (IF ANY)</p>	<p>INDIVIDUAL EARTHING CONNECTIONS COMPLETED FOR I/O CABLES TO SWITCHGEAR TERMINATION BOX</p>	<p>INDIVIDUAL EARTHING CONNECTIONS COMPLETED FOR I/O CABLES TO SWITCHGEAR TERMINATION BOX SECOND PICTURE (IF ANY)</p>

**VERIFIED BY TNB**

**TNB Personnel:**

**Verified at:** 01-03-2026 13:49:34
